



REQUEST FOR INFORMATION FORM

SWML-ENG-001
Revision 0
Page 1 of 3

Project No.:	01-26-020 (26766)	RFI No.:	RFI-126020-011
Date:	August 25, 2026	Discipline:	Mechanical
Project Name:	26766 – BA2107 TLE End-of-Life Replacement		

Subject:	TLE Channel Cover Lifting Lugs
Specifications/Documents/Drawings Referenced or Impacted:	
26766 - CWP-G02 Rev 0.1 - 2021489 – IFC, Scope of Work Section 6.1.9	
Lifting Lug Drawing EA2102D-049 Rev 0.2, “EA-2102D New Lifting Lug Installation” (Work Package, page 92)	

Question or Description of Issue:
Section 6.1.9 of the Construction Work Package directs the contractor to use the existing channel cover lifting lugs to remove TLEs EA-2107A, B and C. Specifically, it states: <i>“Use the existing lifting lug on the top of each TLE’s channel cover to lift existing TLEs tag # EA-2107A, B & C from heater BA-2107. Refer to drawing number EA2102D-049. The cover lifting lugs have a combined vertical lifting capacity of 43,042 lbs. These cover lifting lugs were installed on EA-2107A & B in 2022. One of these covers can be used to replace the cover on EA-2107C after EA-2107A&B have been removed.”</i> Drawing EA2102D-049 Rev. 0.2 indicates that the revised lifting lug arrangement was implemented on the EA-2107B channel in 2022; however, the lifting lug configuration shown on the drawing does not appear to be present in the field. The drawing notes: <i>“This change is implemented in April 2022, when EA-2102D channel is installed on EA-2107B TLE tube section. These lifting lugs have been designed for this configuration only. Any future change must be re-evaluated by engineering.”</i>
Originator’s Recommended Solution:
Please perform a field review to document the existing lifting lug configurations and provide direction on the appropriate lifting points and removal method for the existing TLEs.
Urgency: Medium (3 days)
Originator:
Nitin Joshi Name Signature PC Title August 25, 2026 Date

Response:
Respondent:
Name Signature Title Date



REQUEST FOR INFORMATION FORM

SWML-ENG-001
Revision 0
Page 2 of 3



NOVA Chemicals

Project Development & Implementation Process

Project Number: 26766	Project Manager:	Site: Corunna
Project Name: BA-2107 TLE End of Life		Track: 1

and connected piping is adequately supported prior to TLE guide steel being removed.

- 6.1.5 Provide a temporary support for the "pant leg" assemblies at the inlet (bottom) of each existing exchanger. This may be already completed. Coordinate with project #27495. Temporary support shall be attach to nearby available structural steel that will remain in place for the duration of the TLE installation.
- 6.1.6 The existing VS & BW piping between the Steam Drum and TLEs shall be temporarily supported and disconnected at the TLEs.
- 6.1.7 All piping shall be adequately temporarily supported before removal activities.
- 6.1.8 After removal of instruments and piping connected to each TLE, unbolt the existing anchor bolts from the structural support while TLE is supported by the crane.
- 6.1.9 Use the existing lifting lug on the top of each TLE's channel cover to lift existing TLEs tag # EA-2107A, B & C from heater BA-2107. Refer to drawing number EA2102D-049. The cover lifting lugs have a combined vertical lifting capacity of 43,042 lbs. These cover lifting lugs were installed on EA-2107A & B in 2022. One of these covers can be used to replace the cover on EA-2107C after EA-2107A&B have been removed. The empty weight of each exchanger is 26,400 lbs plus 3,000 lbs of insulation. The contractor shall conduct Magnetic Particle Testing of all the existing lifting lug welds prior to the lift of each TLE and provide report to NOVA.
- 6.1.10 Contractor shall transport the existing TLEs to the cleaning bay then transport to a laydown area designated by NOVA after cleaning. NOVA will clean the existing TLEs but will require the Contractor to assist in handling and connection setup during the cleaning process.
- 6.1.11 NOVA will arrange for the demolition and disposal of the three existing TLEs EA-2107A, B & C at a later date.
- 6.1.12 Installation of New TLEs, EA-2107A,B&C at Heater BA-2107:**
- 6.1.13 Refer to the Drawings List below for the new TLE details.
- 6.1.14 Both shell side and tubeside of each TLE will be filled with 5-7 psig of Nitrogen. Caution shall be exercised to vent the Nitrogen before attempting to remove blind covers and caps. Care shall be taken to preserve TLE internal cleanliness after venting Nitrogen blanket.
- 6.1.15 The Contractor shall supply all materials and labour to insulate each TLE per applicable NOVA Standards and Arvos Insulation Specification number 101491-81-000-IS4. Alkegel Ember with aluminum jacketing shall be used. Use 2 ½" (65mm) thick insulation for the top gas outlet chamber and tube bundle, and 2"(50mm) for the rest of the TLE sections (Riser and Downcomer headers) to be insulated. Nova shall direct work regarding removable insulation blankets. Aluminum jacketing shall be used per



REQUEST FOR INFORMATION FORM


SWML-ENG-001

Revision 0

Page 3 of 3

NOTES:

1. ALL DIMENSIONS IN MILLIMETERS.
2. ALL MODIFICATIONS SHALL BE COMPLETED IN COMPLIANCE WITH TSSA ACT 03/REG. 220/01, CSA B51-2019 AND ASME BPVC SECT. VIII, DIV. 1 - 2021.
3. WELDING SHALL BE COMPLETED IN ACCORDANCE WITH ASME BPVC SECT. IX.
4. PREHEAT TEMPERATURE 400°F (204°C) SHALL BE MAINTAINED DURING WELDING IN ACCORDANCE WITH ASME BPVC SECT. VIII, DIV. 1, PART 4.9.1.
5. POST WELD HEAT TREATMENT SHALL BE COMPLETED AT TEMPERATURE 1250°F (677°C) for 45min. IN ACCORDANCE WITH TABLE UCS-56.4.
6. EACH LUG IS DESIGNED FOR USE WITH CROSBY C-2130 13.5 TON CAPACITY.
7. THE DESIGN LOAD FOR EACH LUG IS 21821 LB. IN-PLANE ONLY.
8. HYDROTEST OF CHANNEL AT 91 PSIG IS REQUIRED AFTER COMPLETION OF WELDING.
9. LIQUID PENETRANT EXAMINATION OF FIRST PASS AND FINAL PASS OF EACH WELD SHALL BE COMPLETED IN ACCORDANCE WITH ASME BPVC SECT. V ARTICLE 6.
10. THIS CHANGE IS IMPLEMENTED IN APRIL 2022, WHEN EA-2102D CHANNEL IS INSTALLED ON EA-2107B TLE TUBE SECTION. THESE LIFTING LUGS HAVE BEEN DESIGNED FOR THIS CONFIGURATION ONLY. ANY FUTURE CHANGE MUST BE RE-EVALUATED BY ENGINEERING.

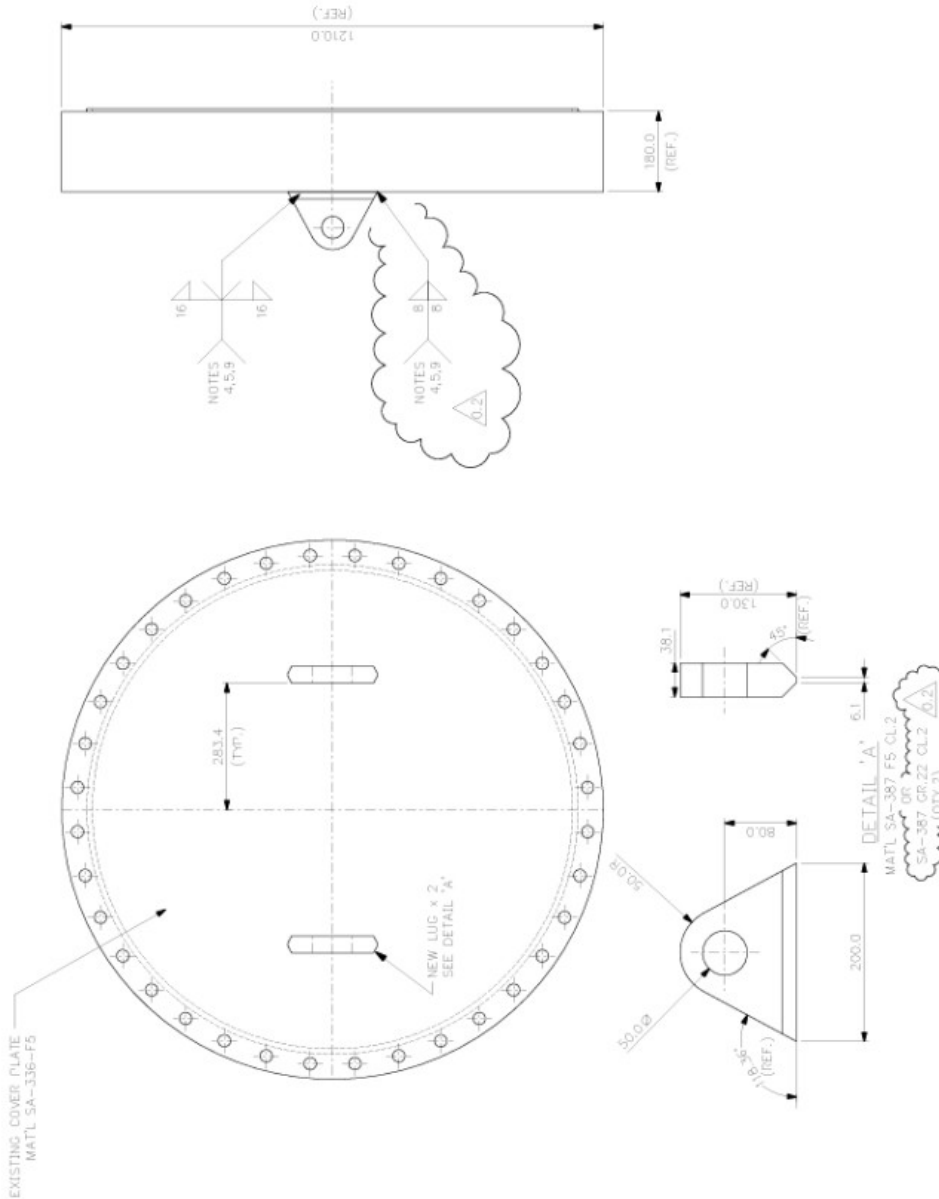

TECSAR
ENGINEERING INC.
FOR INFORMATION ONLY
06/01/2026



Unit 2:100

EA-2102D
NEW LIFTING LUG INSTALLATION

29-25-01

Scale	Portfolio No.	Drawing No.	Rev
3:291360	EA2102D-049	0.2	

REV.	NO.	DATE	REVISIONS	REV.	BY	CHKD.	BY	APP.	BY
0.2		AUG 2022	REVISED MATERIAL - A.F.C. (NOT.#3291360)	KJ	JG				CB
0.1		AUG 2022	APPROVED FOR CONSTRUCTION (NOT.#3291360)	KJ	JG				CB

Notes

1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 32 33 34 35 36 37 38 39 40 41 42 43 44 45 46 47 48 49 50 51 52 53 54 55 56 57 58 59 60 61 62 63 17 AUG 2022 0.2/0.1/0.2/0.3/0.4/0.5/0.6/0.7/0.8/0.9/1.0/1.1/1.2/1.3/1.4/1.5/1.6/1.7/1.8/1.9/2.0/2.1/2.2/2.3/2.4/2.5/2.6/2.7/2.8/2.9/3.0/3.1/3.2/3.3/3.4/3.5/3.6/3.7/3.8/3.9/4.0/4.1/4.2/4.3/4.4/4.5/4.6/4.7/4.8/4.9/5.0/5.1/5.2/5.3/5.4/5.5/5.6/5.7/5.8/5.9 61 62 63 17 AUG 2022 0.2/0.1/0.2/0.3/0.4/0.5/0.6/0.7/0.8/0.9/1.0/1.1/1.2/1.3/1.4/1.5/1.6/1.7/1.8/1.9/2.0/2.1/2.2/2.3/2.4/2.5/2.6/2.7/2.8/2.9/3.0/3.1/3.2/3.3/3.4/3.5/3.6/3.7/3.8/3.9/4.0/4.1/4.2/4.3/4.4/4.5/4.6/4.7/4.8/4.9/5.0/5.1/5.2/5.3/5.4/5.5/5.6/5.7/5.8/5.9
